

1 PROGRAMME BASIS

|                     |                                                                                            |
|---------------------|--------------------------------------------------------------------------------------------|
| Project             | Underground CBRN-Hardened Blast-Resistant Protective Structure and Sentry Post             |
| Location            | Pune, Maharashtra                                                                          |
| Design basis        | Architectural Rev F · Structural Phase 2 Rev A + M1                                        |
| Services packages   | Drainage DR1 · HVAC HV1 · Schedule of Finishes FN1 · Structural CAD SC1                    |
| Programme revision  | WM1 — the R0 master construction schedule, rebuilt                                         |
| Data date / start   | Monday 02 November 2026                                                                    |
| Completion          | Saturday 20 November 2027                                                                  |
| Duration            | 326 working days (384 calendar days, 12.6 months)                                          |
| Activities          | 279, of which 18 milestones, in a 3-level WBS                                              |
| Logic links         | 404 finish-to-start, start-to-start, finish-to-finish and finish-to-finish links with lags |
| Critical activities | 75 activities at total float 0                                                             |
| Calendar            | Six-day week, Mon–Sat, 08:00–17:00 with a one-hour break                                   |

Six-day working week, Monday to Saturday; Sunday non-working. Five date-certain national holidays are non-working. Maharashtra festival holidays are NOT in the calendar because their dates move; the programme carries a stated contingency activity before handover to absorb them. Monsoon (June to September at Pune) is handled by productivity allowances inside the affected durations and by the sequencing rule that the deep excavation and the external tanking are kept out of the monsoon, not by making the calendar non-working.

2 THE SIX DECISIONS THAT SHAPE THIS PROGRAMME

- 1 Blast doors are ordered on day 1. The cast-in frames must be welded into the W6 and W7 cages before those walls are poured, so a 75-day frame lead time sits directly upstream of the wall concrete.
- 2 The pressure slab props stay for 14 days. IS 456 Table 11 requires 14 days for props to a slab spanning over 4.5 m; this one spans 5.000 m clear. Fourteen days of curing plus five of striking sit on the critical path and cannot be compressed.
- 3 The roof is cast before the walls are backfilled. Backfilling against a 3.2 m unpropped wall is what the 15.41 kPa/m lateral gradient forbids; the roof provides the prop.
- 4 The engineered cover is a six-layer structure, not a fill operation. It contains a 200 mm M30 burster slab that must be formed, reinforced, poured and cured inside the cover.
- 5 The sentry post starts only after the rock breaking finishes. No green concrete stands within 10 m of a hydraulic breaker, and the post carries 118 days of float, which makes it the natural place to absorb delay and redeploy labour.
- 6 Nothing is programmed against a fabricated festival-holiday date. The calendar carries only date-certain national holidays; a 10-day contingency activity before handover absorbs the movable ones.

5 WHAT THIS PROGRAMME ASSUMES, AND WHAT MUST BE CONFIRMED BEFORE IT CAN BE RELIED ON

|       |                                                                                                                                                                                                            |
|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| WM-P1 | Project start Monday 2 November 2026 is carried over from the supplied R0 master construction schedule. It is a planning date, not a contractual one.                                                      |
| WM-P2 | Durations are built from the quantities derived in the BOQ and from output rates typical of Indian sites; they are ASSUMED and must be re-tested against the appointed contractor's resources.             |
| WM-P3 | The rockhead is ASSUMED in the master at (-)1.500 to (-)2.000. Rock excavation is programmed at the mean, 994 m3. At the shallow bound it rises to 1043 m3 and the excavation lengthens by about a day.    |
| WM-P4 | The design groundwater table (-)2.000 is ASSUMED. A1080 puts monsoon monitoring on the critical path deliberately: if the water is higher, the dewatering, the tanking and the flotation check all change. |
| WM-P5 | No blasting is assumed. Rock is removed by hydraulic breaker because the sentry post founds on the same rock within 10 m.                                                                                  |
| WM-P6 | Vendor lead times for the blast doors, filter trains, blast valves and the EMP enclosure are ASSUMED. They are the longest single risk in the programme and must be replaced by quoted times at tender.    |
| WM-P7 | Festival holidays are not in the calendar; A14098 carries ten working days of contingency in their place.                                                                                                  |
| WM-P8 | The berm, the access route and the concealment works have no site plan behind them, so their durations are indicative only.                                                                                |

3 MILESTONE REGISTER

| REF  | ACT    | MILESTONE                                     | DATE      | FLOAT | STATUS   |
|------|--------|-----------------------------------------------|-----------|-------|----------|
| M-01 | A1025  | Site possession and commencement              | 07 Nov 26 | 0 d   | CRITICAL |
| M-02 | A1065  | Mobilisation complete                         | 26 Nov 26 | 8 d   |          |
| M-03 | A1175  | All long-lead protective items ordered        | 23 Feb 27 | 230 d |          |
| M-04 | A2090  | Excavation complete, formation approved       | 06 Feb 27 | 0 d   | CRITICAL |
| M-05 | A3085  | Mat foundation cast                           | 15 Mar 27 | 213 d |          |
| M-06 | A3160  | Perimeter and protective walls complete       | 05 May 27 | 170 d |          |
| M-07 | A4085  | Pressure slab cast — key structural milestone | 28 Jun 27 | 26 d  |          |
| M-08 | A6055  | Buried envelope watertight — tanking complete | 05 Aug 27 | 91 d  |          |
| M-09 | A7065  | Overburden complete — structure buried        | 10 Sep 27 | 0 d   | CRITICAL |
| M-10 | A8125  | Sentry post frame complete                    | 20 Apr 27 | 182 d |          |
| M-11 | A8165  | Sentry post brick masonry complete            | 28 Apr 27 | 175 d |          |
| M-12 | A8215  | Sentry post complete                          | 11 Jun 27 | 109 d |          |
| M-13 | A9060  | CBRN plant installed                          | 26 Aug 27 | 23 d  |          |
| M-14 | A10065 | Drainage installed                            | 16 Sep 27 | 13 d  |          |
| M-15 | A11060 | Electrical installation complete              | 02 Sep 27 | 22 d  |          |
| M-16 | A12070 | Internal finishes complete                    | 18 Sep 27 | 53 d  |          |
| M-17 | A13050 | External works and concealment complete       | 18 Oct 27 | 0 d   | CRITICAL |
| M-18 | A14105 | PRACTICAL COMPLETION AND HANDOVER             | 20 Nov 27 | 0 d   | CRITICAL |

4 CRITICAL PATH — THE CONTROLLING CHAIN

- 1 PRE-CONSTRUCTION AND ENABLING WORKS — enters the path at A1010 on 02 Nov 26
- 2 SITE PREPARATION AND EARTHWORKS — enters the path at A2025 on 11 Dec 26
- 3 MAIN UNDERGROUND SHELTER — SUBSTRUCTURE — enters the path at A3010 on 06 Feb 27
- 4 MAIN UNDERGROUND SHELTER — PRESSURE SLAB — enters the path at A4010 on 05 May 27
- 6 WATERPROOFING — enters the path at A6030 on 23 Jul 27
- 7 BACKFILL, ENGINEERED COVER AND OVERBURDEN — enters the path at A7025 on 05 Aug 27
- 13 EXTERNAL WORKS, CONCEALMENT AND RESTORATION — enters the path at A13010 on 10 Sep 27
- 14 TESTING, COMMISSIONING AND HANDOVER — enters the path at A14080 on 18 Oct 27


The controlling chain is: site possession and the confirmatory site investigation, which must close the ASSUMED groundwater level before the excavation support can be designed; rock excavation; formation approval; the external tanking; the mat; the perimeter and protective walls; the pressure slab with its 14-day prop period; the roof membrane; the six-layer engineered cover including the burster slab; the external works and concealment; and finally snagging, rectification and handover. Every one of the eighteen milestones is either on that chain or hangs from it.

6 PEAK RESOURCE REQUIREMENT AND FILE FORMAT

| GROUP  | RESOURCE                 | COMPOSITION                       | PEAK | DRIVEN BY                                                        |
|--------|--------------------------|-----------------------------------|------|------------------------------------------------------------------|
| Labour | Bar bender gang          | 1 gang = 1 fitter + 3 helpers     | 4    | Peak on the pressure slab: 20.5 t of T25 at 150 both faces both  |
| Labour | Carpenter gang           | 1 gang = 1 carpenter + 2 helpers  | 4    | Peak on the pressure slab falsework, 104 m2 of deck at 3.200 m   |
| Labour | Concrete gang            | 1 gang = 1 mason + 6 helpers      | 2    | Continuous pours: mat 85 m3, pressure slab 112 m3                |
| Labour | Mason gang               | 1 gang = 1 mason + 2 helpers      | 3    | SENTRY POST BRICK MASONRY; screeds; floor finishes; chambers     |
| Labour | Plasterer gang           | 1 gang = 1 plasterer + 1 helper   | 2    | Sentry post internal and external plaster                        |
| Labour | Painter gang             | 1 gang = 1 painter + 1 helper     | 2    | Sealed washable coatings internally; sentry post painting        |
| Labour | Waterproofing gang       | specialist, 1 gang = 4 No.        | 4    | Tanking is a specialist trade — 532 m2 of continuous membrane    |
| Labour | Electrician gang         | 1 gang = 1 electrician + 1 helper | 3    | Conduits, cabling, earthing, EMP bonding                         |
| Labour | Plumber gang             | 1 gang = 1 plumber + 1 helper     | 2    | Drainage, sumps, rising mains                                    |
| Labour | HVAC fitter              | 1 gang = 1 fitter + 1 helper      | 2    | Ductwork, blast valves, CBRN plant                               |
| Labour | Unskilled gang           | general labour                    | 20   | Curing, handling, backfill, cleaning                             |
| Labour | Specialist subcontractor | as required                       | 1    | EMP enclosure, blast doors, CBRN commissioning, gas-tightness te |
| Plant  | Excavator                | 0.9 m3 tracked                    | 2    | Bulk excavation, backfill, cover                                 |
| Plant  | Rock breaker             | hydraulic, excavator mounted      | 2    | 994 m3 of basalt; NO BLASTING permitted near the sentry post     |
| Plant  | Tipper                   | 10 t                              | 4    | Spoil haulage; peak during rock excavation                       |
| Plant  | Dozer/grader             | 1 No.                             | 1    | Berm, regrading, access                                          |
| Plant  | Vibratory roller         | 1 No.                             | 1    | Backfill and cover compaction to 95 % MDD                        |
| Plant  | Plate compactor          | 2 No.                             | 2    | Confined backfill in 250 layers                                  |
| Plant  | Concrete pump            | boom pump                         | 1    | 112 m3 continuous pour to the pressure slab                      |
| Plant  | Transit mixer            | 6 m3                              | 4    | Peak on the pressure slab pour                                   |
| Plant  | Crane                    | 20 t mobile                       | 1    | Blast doors, filter trains, EMP enclosure, spiral stair          |
| Plant  | Dewatering pumps         | duty + standby                    | 2    | Continuous through the substructure; GWT (-)2.000 is ASSUMED     |
| Plant  | Scaffolding              | tube and fitting                  | 1    | Slab falsework, masonry, plaster; IS 3696 / IS 4014              |
| Plant  | Welding set              | 2 No.                             | 2    | EMP straps and blast door frames welded to the reinforcement cag |


PROGRAMME FILE FORMAT

The editable master programme accompanying this PDF is Underground\_Shelter\_Final\_Works\_Programme.xml, written in MSPDI — Microsoft Project's own published XML schema. Microsoft Project opens it directly and File > Save As > Project (\*.mpp) produces the binary .mpp. The native .mpp format is undocumented and can only be written by Microsoft Project itself, so it is not produced here rather than being imitated. The XML carries the full WBS, all 279 activities, all 404 logic links with their lags, the six-day calendar with its exceptions, 33 resources and 426 assignments; it was verified by reading it back with MPXJ and comparing every date against the critical-path calculation.

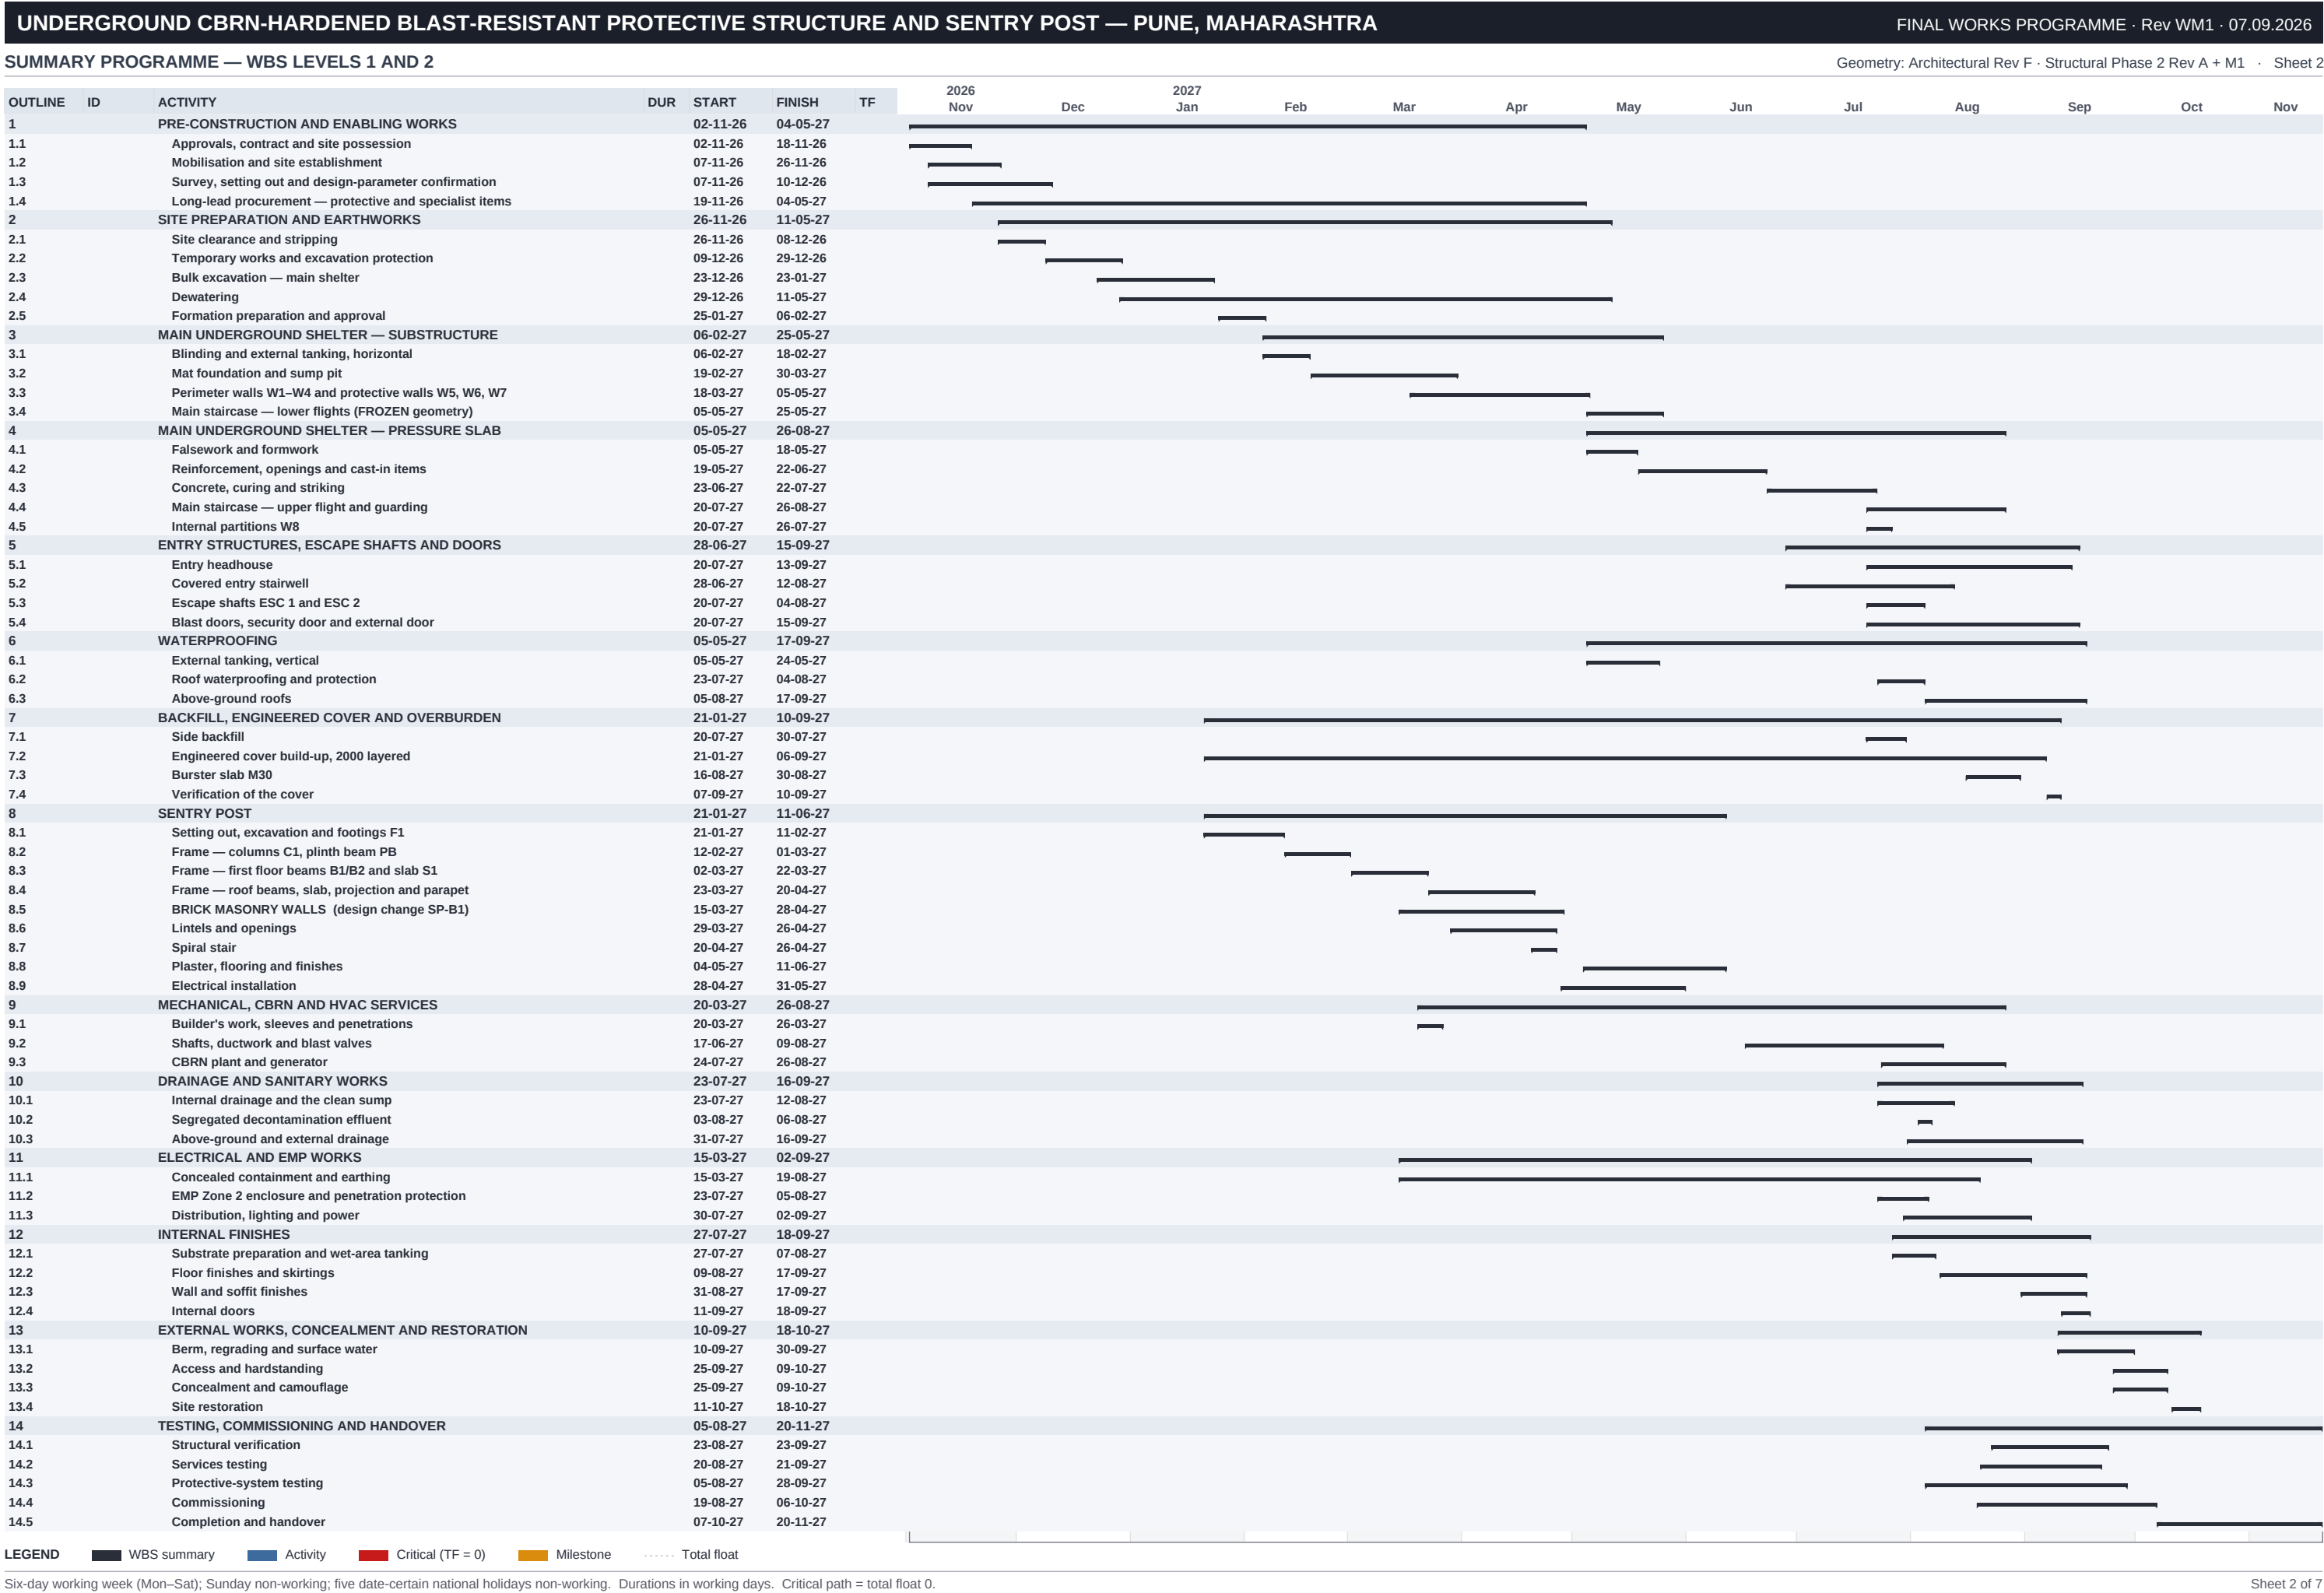

| UNDERGROUND CBRN-HARDENED BLAST-RESISTANT PROTECTIVE STRUCTURE AND SENTRY POST — PUNE, MAHARASHTRA |       |                                                                              |     |          |          |     |             |          |                   |           |             |     |     |     | FINAL WORKS PROGRAMME · Rev WM1 · 07.09.2026                            |     |     |     |     |
|----------------------------------------------------------------------------------------------------|-------|------------------------------------------------------------------------------|-----|----------|----------|-----|-------------|----------|-------------------|-----------|-------------|-----|-----|-----|-------------------------------------------------------------------------|-----|-----|-----|-----|
| DETAILED WORKS PROGRAMME (1 OF 5)                                                                  |       |                                                                              |     |          |          |     |             |          |                   |           |             |     |     |     | Geometry: Architectural Rev F · Structural Phase 2 Rev A + M1 · Sheet 3 |     |     |     |     |
| OUTLINE                                                                                            | ID    | ACTIVITY                                                                     | DUR | START    | FINISH   | TF  | 2026        | Dec      | 2027              | Feb       | Mar         | Apr | May | Jun | Jul                                                                     | Aug | Sep | Oct | Nov |
|                                                                                                    |       |                                                                              |     |          |          |     | Nov         |          | Jan               |           |             |     |     |     |                                                                         |     |     |     |     |
| 1                                                                                                  |       | PRE-CONSTRUCTION AND ENABLING WORKS                                          |     | 02-11-26 | 04-05-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.1                                                                                                |       | Approvals, contract and site possession                                      |     | 02-11-26 | 18-11-26 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.1.1                                                                                              | A1010 | Contract award, signature and site possession                                | 5   | 02-11-26 | 06-11-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.1.2                                                                                              | A1015 | Statutory and Service approvals; security clearance of the workforce         | 10  | 02-11-26 | 12-11-26 | 19  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.1.3                                                                                              | A1020 | Contractor's programme, method statements and quality plan — approval        | 10  | 07-11-26 | 18-11-26 | 19  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.1.4                                                                                              | A1025 | MILESTONE: Site possession and commencement                                  |     | 07-11-26 | 07-11-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2                                                                                                |       | Mobilisation and site establishment                                          |     | 07-11-26 | 26-11-26 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.1                                                                                              | A1030 | Site office, stores, labour accommodation and first-aid post                 | 8   | 07-11-26 | 16-11-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.2                                                                                              | A1035 | Site boundary, security fencing, gate and access control                     | 6   | 07-11-26 | 13-11-26 | 13  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.3                                                                                              | A1040 | Temporary water supply, storage and distribution                             | 5   | 10-11-26 | 14-11-26 | 17  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.4                                                                                              | A1045 | Temporary power supply and site distribution board                           | 5   | 10-11-26 | 14-11-26 | 17  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.5                                                                                              | A1050 | Concrete supply arrangements and site testing laboratory                     | 8   | 17-11-26 | 25-11-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.6                                                                                              | A1055 | Material stacking areas, reinforcement yard and bar-bending area             | 5   | 17-11-26 | 21-11-26 | 11  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.7                                                                                              | A1060 | Plant mobilisation — excavator, breakers, crane, pumps, compactors           | 5   | 14-11-26 | 19-11-26 | 13  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.2.8                                                                                              | A1065 | MILESTONE: Mobilisation complete                                             |     | 26-11-26 | 26-11-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3                                                                                                |       | Survey, setting out and design-parameter confirmation                        |     | 07-11-26 | 10-12-26 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.1                                                                                              | A1070 | Topographic survey, benchmarks and establishment of the site grid            | 4   | 07-11-26 | 11-11-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.2                                                                                              | A1075 | Confirmatory site investigation — boreholes, rockhead, red-bole seams        | 12  | 12-11-26 | 25-11-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.3                                                                                              | A1080 | Monsoon groundwater monitoring — confirm the design GWT (-)2.000             | 20  | 12-11-26 | 04-12-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.4                                                                                              | A1085 | Percolation test for the soak pits — IS 2470 (Part 2) Cl. 4                  | 5   | 26-11-26 | 01-12-26 | 3   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.5                                                                                              | A1090 | Issue confirmed geotechnical parameters to the designer                      | 5   | 05-12-26 | 10-12-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.6                                                                                              | A1095 | Setting out — shelter box, headhouse and covered stairwell                   | 3   | 12-11-26 | 14-11-26 | 13  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.7                                                                                              | A1100 | Setting out — sentry post, not less than 10 m clear of the excavation        | 2   | 16-11-26 | 17-11-26 | 13  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.3.8                                                                                              | A1105 | Setting-out check and independent verification                               | 2   | 18-11-26 | 19-11-26 | 13  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4                                                                                                |       | Long-lead procurement — protective and specialist items                      |     | 19-11-26 | 04-05-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.1                                                                                              | A1110 | Blast doors 1 and 2 — specification, enquiry and technical evaluation        | 15  | 19-11-26 | 05-12-26 | 19  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.2                                                                                              | A1115 | Blast doors — order placement                                                | 5   | 07-12-26 | 11-12-26 | 19  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.3                                                                                              | A1120 | Blast door cast-in FRAMES — manufacture and delivery                         | 75  | 12-12-26 | 11-03-27 | 19  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.4                                                                                              | A1122 | Blast door LEAVES — manufacture, factory proof test and shipment             | 120 | 12-12-26 | 04-05-27 | 116 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.5                                                                                              | A1130 | CBRN filter trains AHU-1/AHU-2 — enquiry and order                           | 20  | 19-11-26 | 11-12-26 | 115 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.6                                                                                              | A1135 | CBRN filter trains — manufacture and delivery                                | 100 | 12-12-26 | 09-04-27 | 115 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.7                                                                                              | A1140 | Blast valves, 5 No. — enquiry and order                                      | 20  | 19-11-26 | 11-12-26 | 131 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.8                                                                                              | A1145 | Blast valves and sleeves — manufacture and delivery                          | 100 | 12-12-26 | 09-04-27 | 131 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.9                                                                                              | A1150 | EMP Zone 2 shielded enclosure — specialist enquiry and order                 | 25  | 19-11-26 | 17-12-26 | 148 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.10                                                                                             | A1155 | EMP Zone 2 enclosure — manufacture and delivery                              | 80  | 18-12-26 | 23-03-27 | 148 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.11                                                                                             | A1160 | Generator 15 kVA — enquiry, order and delivery                               | 60  | 19-11-26 | 29-01-27 | 195 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.12                                                                                             | A1165 | Armoured vision panels, 8 No. — enquiry, order and delivery                  | 80  | 19-11-26 | 22-02-27 | 173 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.13                                                                                             | A1170 | Submersible pumps and drainage plant — order and delivery                    | 45  | 19-11-26 | 11-01-27 | 214 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.14                                                                                             | A1172 | Reinforcement Fe500D — order, mill certificates and delivery                 | 30  | 19-11-26 | 23-12-26 | 47  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.15                                                                                             | A1174 | Waterproofing system — approval of the proprietary system and order          | 30  | 19-11-26 | 23-12-26 | 39  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.16                                                                                             | A1176 | Modular bricks to IS 1077 — source approval, testing and order               | 20  | 19-11-26 | 11-12-26 | 198 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 1.4.17                                                                                             | A1175 | MILESTONE: All long-lead protective items ordered                            |     | 23-02-27 | 23-02-27 | 230 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2                                                                                                  |       | SITE PREPARATION AND EARTHWORKS                                              |     | 26-11-26 | 11-05-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.1                                                                                                |       | Site clearance and stripping                                                 |     | 26-11-26 | 08-12-26 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.1.1                                                                                              | A2010 | Site clearance, grubbing and removal of plants and shrubs                    | 4   | 26-11-26 | 30-11-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.1.2                                                                                              | A2015 | Strip topsoil 150 and stockpile for the concealment layer                    | 3   | 01-12-26 | 03-12-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.1.3                                                                                              | A2020 | Site levelling, temporary haul road and hardstanding                         | 4   | 04-12-26 | 08-12-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.2                                                                                                |       | Temporary works and excavation protection                                    |     | 09-12-26 | 29-12-26 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.2.1                                                                                              | A2025 | Design and approval of excavation support and slope treatment                | 10  | 11-12-26 | 22-12-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.2.2                                                                                              | A2030 | Surface water cut-off drains and interceptor around the excavation           | 4   | 09-12-26 | 12-12-26 | 8   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.2.3                                                                                              | A2035 | Excavation edge protection, barriers, signage and access ladders             | 3   | 26-12-26 | 29-12-26 | 30  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.3                                                                                                |       | Bulk excavation — main shelter                                               |     | 23-12-26 | 23-01-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.3.1                                                                                              | A2040 | Excavation in soil and weathered overburden to rockhead                      | 4   | 23-12-26 | 28-12-26 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.3.2                                                                                              | A2045 | Rock excavation by hydraulic breaker, (-)1.750 to (-)4.000                   | 9   | 29-12-26 | 07-01-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.3.3                                                                                              | A2050 | Rock excavation by hydraulic breaker, (-)4.000 to (-)6.800                   | 11  | 08-01-27 | 20-01-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.3.4                                                                                              | A2055 | Excavation for the covered entry stairwell approach                          | 5   | 14-01-27 | 19-01-27 | 160 |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.3.5                                                                                              | A2060 | Excavation in rock for the sump pit, to (-)8.100                             | 3   | 21-01-27 | 23-01-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.4                                                                                                |       | Dewatering                                                                   |     | 29-12-26 | 11-05-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.4.1                                                                                              | A2065 | Install and commission the construction dewatering system                    | 3   | 29-12-26 | 31-12-26 | 73  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.4.2                                                                                              | A2070 | Dewatering — continuous through the substructure works                       | 110 | 01-01-27 | 11-05-27 | 73  |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.5                                                                                                |       | Formation preparation and approval                                           |     | 25-01-27 | 06-02-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.5.1                                                                                              | A2075 | Trim, dress and clean the formation; remove loose rock                       | 4   | 25-01-27 | 29-01-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.5.2                                                                                              | A2080 | Inspect for red-bole and vesicular seams; over-excavate and replace with M15 | 4   | 30-01-27 | 03-02-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.5.3                                                                                              | A2085 | HOLD POINT: formation inspection and approval by the Engineer                | 2   | 04-02-27 | 05-02-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 2.5.4                                                                                              | A2090 | MILESTONE: excavation complete, formation approved                           |     | 06-02-27 | 06-02-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 3                                                                                                  |       | MAIN UNDERGROUND SHELTER — SUBSTRUCTURE                                      |     | 06-02-27 | 25-05-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 3.1                                                                                                |       | Blinding and external tanking, horizontal                                    |     | 06-02-27 | 18-02-27 |     |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 3.1.1                                                                                              | A3010 | Blinding PCC M15 100 thk under the mat                                       | 3   | 06-02-27 | 09-02-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 3.1.2                                                                                              | A3015 | Blinding PCC M15 to the sump pit                                             | 1   | 06-02-27 | 06-02-27 | 2   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 3.1.3                                                                                              | A3020 | External tanking WP-01 — horizontal, on the blinding                         | 5   | 10-02-27 | 15-02-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| 3.1.4                                                                                              | A3025 | Protection layer to the horizontal tanking                                   | 2   | 16-02-27 | 17-02-27 | 0   |             |          |                   |           |             |     |     |     |                                                                         |     |     |     |     |
| LEGEND                                                                                             |       |                                                                              |     |          |          |     | WBS summary | Activity | Critical (TF = 0) | Milestone | Total float |     |     |     |                                                                         |     |     |     |     |

| UNDERGROUND CBRN-HARDENED BLAST-RESISTANT PROTECTIVE STRUCTURE AND SENTRY POST — PUNE, MAHARASHTRA |       |                                                                                 |     |          |          |     |                                                                                    |     |             |     |     |     |     | FINAL WORKS PROGRAMME · Rev WM1 · 07.09.2026                            |     |     |     |     |     |  |  |  |  |  |  |  |  |
|----------------------------------------------------------------------------------------------------|-------|---------------------------------------------------------------------------------|-----|----------|----------|-----|------------------------------------------------------------------------------------|-----|-------------|-----|-----|-----|-----|-------------------------------------------------------------------------|-----|-----|-----|-----|-----|--|--|--|--|--|--|--|--|
| DETAILED WORKS PROGRAMME (2 OF 5)                                                                  |       |                                                                                 |     |          |          |     |                                                                                    |     |             |     |     |     |     | Geometry: Architectural Rev F · Structural Phase 2 Rev A + M1 · Sheet 4 |     |     |     |     |     |  |  |  |  |  |  |  |  |
| OUTLINE                                                                                            | ID    | ACTIVITY                                                                        | DUR | START    | FINISH   | TF  | 2026<br>Nov                                                                        | Dec | 2027<br>Jan | Feb | Mar | Apr | May | Jun                                                                     | Jul | Aug | Sep | Oct | Nov |  |  |  |  |  |  |  |  |
| 3.1.5                                                                                              | A3030 | HOLD POINT: tanking integrity inspection before covering                        | 1   | 18-02-27 | 18-02-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2                                                                                                |       | Mat foundation and sump pit                                                     |     | 19-02-27 | 30-03-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.1                                                                                              | A3035 | Sump pit SU-01 — formwork and reinforcement below the mat                       | 4   | 19-02-27 | 23-02-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.2                                                                                              | A3040 | Mat reinforcement — bottom curtain T16 @ 150 each way                           | 4   | 19-02-27 | 23-02-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.3                                                                                              | A3045 | Wall starter bars, 900 leg into the mat; kickers set out                        | 3   | 24-02-27 | 26-02-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.4                                                                                              | A3050 | Mat links T12 @ 250 x 250 grid, chairs and spacers                              | 3   | 27-02-27 | 02-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.5                                                                                              | A3055 | Mat reinforcement — top curtain T16 @ 150 each way                              | 4   | 03-03-27 | 06-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.6                                                                                              | A3060 | Mat edge formwork and U-bars; waterstops at the kicker                          | 3   | 08-03-27 | 10-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.7                                                                                              | A3065 | Cast-in items — drainage BW-01, sleeves, earth pits, EMP straps                 | 3   | 08-03-27 | 10-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.8                                                                                              | A3070 | HOLD POINT: mat reinforcement, cover and cast-in inspection                     | 1   | 11-03-27 | 11-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.9                                                                                              | A3075 | Concrete mat 600 M35 and sump pit — single continuous pour                      | 2   | 12-03-27 | 13-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.10                                                                                             | A3080 | Curing of the mat — 14 days continuous                                          | 14  | 15-03-27 | 30-03-27 | 1   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.2.11                                                                                             | A3085 | MILESTONE: mat foundation cast                                                  |     | 15-03-27 | 15-03-27 | 213 |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3                                                                                                |       | Perimeter walls W1–W4 and protective walls W5, W6, W7                           |     | 18-03-27 | 05-05-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.1                                                                                              | A3090 | Wall reinforcement W1–W4 — both curtains T16 @ 150 each face, each way          | 12  | 18-03-27 | 31-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.2                                                                                              | A3095 | Wall reinforcement W5, W6, W7 incl. blast door jambs and header                 | 6   | 25-03-27 | 31-03-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.3                                                                                              | A3100 | Haunch reinforcement 500 x 500, diagonal T20 @ 150, wall/mat junction           | 3   | 20-03-27 | 23-03-27 | 7   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.4                                                                                              | A3105 | Set and align the BLAST DOOR FRAMES in W6 and W7; weld to the cage              | 4   | 01-04-27 | 05-04-27 | 2   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.5                                                                                              | A3110 | Concealed conduits, sleeves and penetrations cast into the walls                | 5   | 01-04-27 | 06-04-27 | 1   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.6                                                                                              | A3115 | Wall formwork — lift 1, (-)6.100 to (-)4.500                                    | 6   | 01-04-27 | 07-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.7                                                                                              | A3120 | HOLD POINT: wall reinforcement, frames and cover inspection — lift 1            | 1   | 08-04-27 | 08-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.8                                                                                              | A3125 | Concrete walls — lift 1, M35                                                    | 2   | 09-04-27 | 10-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.9                                                                                              | A3130 | Curing lift 1; strike vertical formwork after 24 h minimum                      | 7   | 12-04-27 | 19-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.10                                                                                             | A3135 | Wall formwork — lift 2, (-)4.500 to (-)2.900                                    | 6   | 15-04-27 | 21-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.11                                                                                             | A3140 | HOLD POINT: wall reinforcement and cover inspection — lift 2                    | 1   | 22-04-27 | 22-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.12                                                                                             | A3145 | Concrete walls — lift 2, M35                                                    | 2   | 23-04-27 | 24-04-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.13                                                                                             | A3150 | Curing lift 2 and strike wall formwork                                          | 7   | 26-04-27 | 04-05-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.14                                                                                             | A3155 | Construction joint preparation — two waterstops and welded EMP strap            | 3   | 12-04-27 | 14-04-27 | 6   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.3.15                                                                                             | A3160 | MILESTONE: perimeter and protective walls complete                              |     | 05-05-27 | 05-05-27 | 170 |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.4                                                                                                |       | Main staircase — lower flights (FROZEN geometry)                                |     | 05-05-27 | 25-05-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.4.1                                                                                              | A3165 | Main staircase — formwork to flights 1 and 2 and landings L1, L2                | 5   | 05-05-27 | 10-05-27 | 113 |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.4.2                                                                                              | A3170 | Main staircase — reinforcement, flights T12 @ 150, landings T12 @ 125           | 4   | 11-05-27 | 14-05-27 | 113 |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.4.3                                                                                              | A3175 | Main staircase — concrete flights 1 and 2 and landings, M35                     | 2   | 15-05-27 | 17-05-27 | 113 |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 3.4.4                                                                                              | A3180 | Main staircase — curing and strike, lower flights                               | 7   | 18-05-27 | 25-05-27 | 113 |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4                                                                                                  |       | MAIN UNDERGROUND SHELTER — PRESSURE SLAB                                        |     | 05-05-27 | 26-08-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.1                                                                                                |       | Falsework and formwork                                                          |     | 05-05-27 | 18-05-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.1.1                                                                                              | A4010 | Falsework and soffit deck to the pressure slab, 3.200 m height                  | 8   | 05-05-27 | 13-05-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.1.2                                                                                              | A4015 | Edge formwork, stair void and escape shaft box-outs                             | 4   | 14-05-27 | 18-05-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2                                                                                                |       | Reinforcement, openings and cast-in items                                       |     | 19-05-27 | 22-06-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.1                                                                                              | A4020 | Pressure slab — bottom curtain T25 @ 150 each way                               | 6   | 19-05-27 | 25-05-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.2                                                                                              | A4025 | Opening trimmers — stair void 6-T25 top and bottom; re-entrant corners 4-T25 at | 4   | 26-05-27 | 29-05-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.3                                                                                              | A4030 | Escape shaft collar trimmers 5-T25 each side/face/direction; hoops and radials  | 4   | 31-05-27 | 03-06-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.4                                                                                              | A4035 | Local thickenings 900 to 1200 at the shafts and the void free edge              | 3   | 01-06-27 | 03-06-27 | 16  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.5                                                                                              | A4040 | Band beneath headhouse wall HW3 — 4-T25 extra top and bottom in a 1200 band     | 2   | 31-05-27 | 01-06-27 | 18  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.6                                                                                              | A4045 | Links T12 4-leg @ 250 in the end 1500; 2-leg @ 300 mid                          | 5   | 04-06-27 | 09-06-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.7                                                                                              | A4050 | Pressure slab — top curtain T25 @ 150 each way                                  | 6   | 10-06-27 | 16-06-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.8                                                                                              | A4055 | Wall/roof haunches 500 x 500, diagonal T20 @ 150                                | 3   | 12-06-27 | 15-06-27 | 6   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.9                                                                                              | A4060 | Cast-in — blast valve sleeves, duct and pipe penetrations, EMP straps           | 5   | 17-06-27 | 22-06-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.10                                                                                             | A4065 | Escape shaft collar starter bars                                                | 2   | 17-06-27 | 18-06-27 | 3   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.2.11                                                                                             | A4067 | Concealed electrical conduits and boxes cast into the slab                      | 4   | 07-06-27 | 10-06-27 | 10  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3                                                                                                |       | Concrete, curing and striking                                                   |     | 23-06-27 | 22-07-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3.1                                                                                              | A4070 | HOLD POINT: pressure slab pre-pour inspection — reinforcement, cover, cast-ins  | 2   | 23-06-27 | 24-06-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3.2                                                                                              | A4075 | Concrete pressure slab 900 M35 — single continuous pour, 112 m3                 | 2   | 25-06-27 | 26-06-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3.3                                                                                              | A4080 | Curing of the pressure slab — 14 days continuous                                | 14  | 28-06-27 | 13-07-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3.4                                                                                              | A4085 | MILESTONE: pressure slab cast — the key structural milestone                    |     | 28-06-27 | 28-06-27 | 26  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3.5                                                                                              | A4090 | Strike soffit formwork and props — props to remain 14 days                      | 5   | 14-07-27 | 19-07-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.3.6                                                                                              | A4095 | Make good, hack and prepare the soffit                                          | 3   | 20-07-27 | 22-07-27 | 0   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.4                                                                                                |       | Main staircase — upper flight and guarding                                      |     | 20-07-27 | 26-08-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.4.1                                                                                              | A4110 | Main staircase — flight 3 to the top of the pressure slab (-)2.000              | 6   | 20-07-27 | 26-07-27 | 66  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.4.2                                                                                              | A4115 | Main staircase — handrails and guarding 1100 high                               | 4   | 23-08-27 | 26-08-27 | 43  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.5                                                                                                |       | Internal partitions W8                                                          |     | 20-07-27 | 26-07-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 4.5.1                                                                                              | A4100 | Internal partitions W8, 4 No., 110 thk with A252 mesh both faces                | 6   | 20-07-27 | 26-07-27 | 7   |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5                                                                                                  |       | ENTRY STRUCTURES, ESCAPE SHAFTS AND DOORS                                       |     | 28-06-27 | 15-09-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1                                                                                                |       | Entry headhouse                                                                 |     | 20-07-27 | 13-09-27 |     |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.1                                                                                              | A5010 | Headhouse — wall starters, kicker and setting out on the pressure slab          | 3   | 20-07-27 | 22-07-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.2                                                                                              | A5015 | Headhouse wall reinforcement HW1–HW4, T16 @ 150 EF EW, T12 4L @ 250             | 6   | 23-07-27 | 29-07-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.3                                                                                              | A5020 | Inner security door frame in HW2 — cast in and welded to the cage               | 2   | 30-07-27 | 31-07-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.4                                                                                              | A5025 | Headhouse wall formwork                                                         | 5   | 02-08-27 | 06-08-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.5                                                                                              | A5030 | HOLD POINT: headhouse wall inspection                                           | 1   | 07-08-27 | 07-08-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.6                                                                                              | A5035 | Concrete headhouse walls 400 M35                                                | 1   | 09-08-27 | 09-08-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| 5.1.7                                                                                              | A5040 | Curing and strike — headhouse walls                                             | 5   | 10-08-27 | 14-08-27 | 13  |                                                                                    |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |
| LEGEND                                                                                             |       |                                                                                 |     |          |          |     | ■ WBS summary   ■ Activity   ■ Critical (TF = 0)   ■ Milestone   ..... Total float |     |             |     |     |     |     |                                                                         |     |     |     |     |     |  |  |  |  |  |  |  |  |

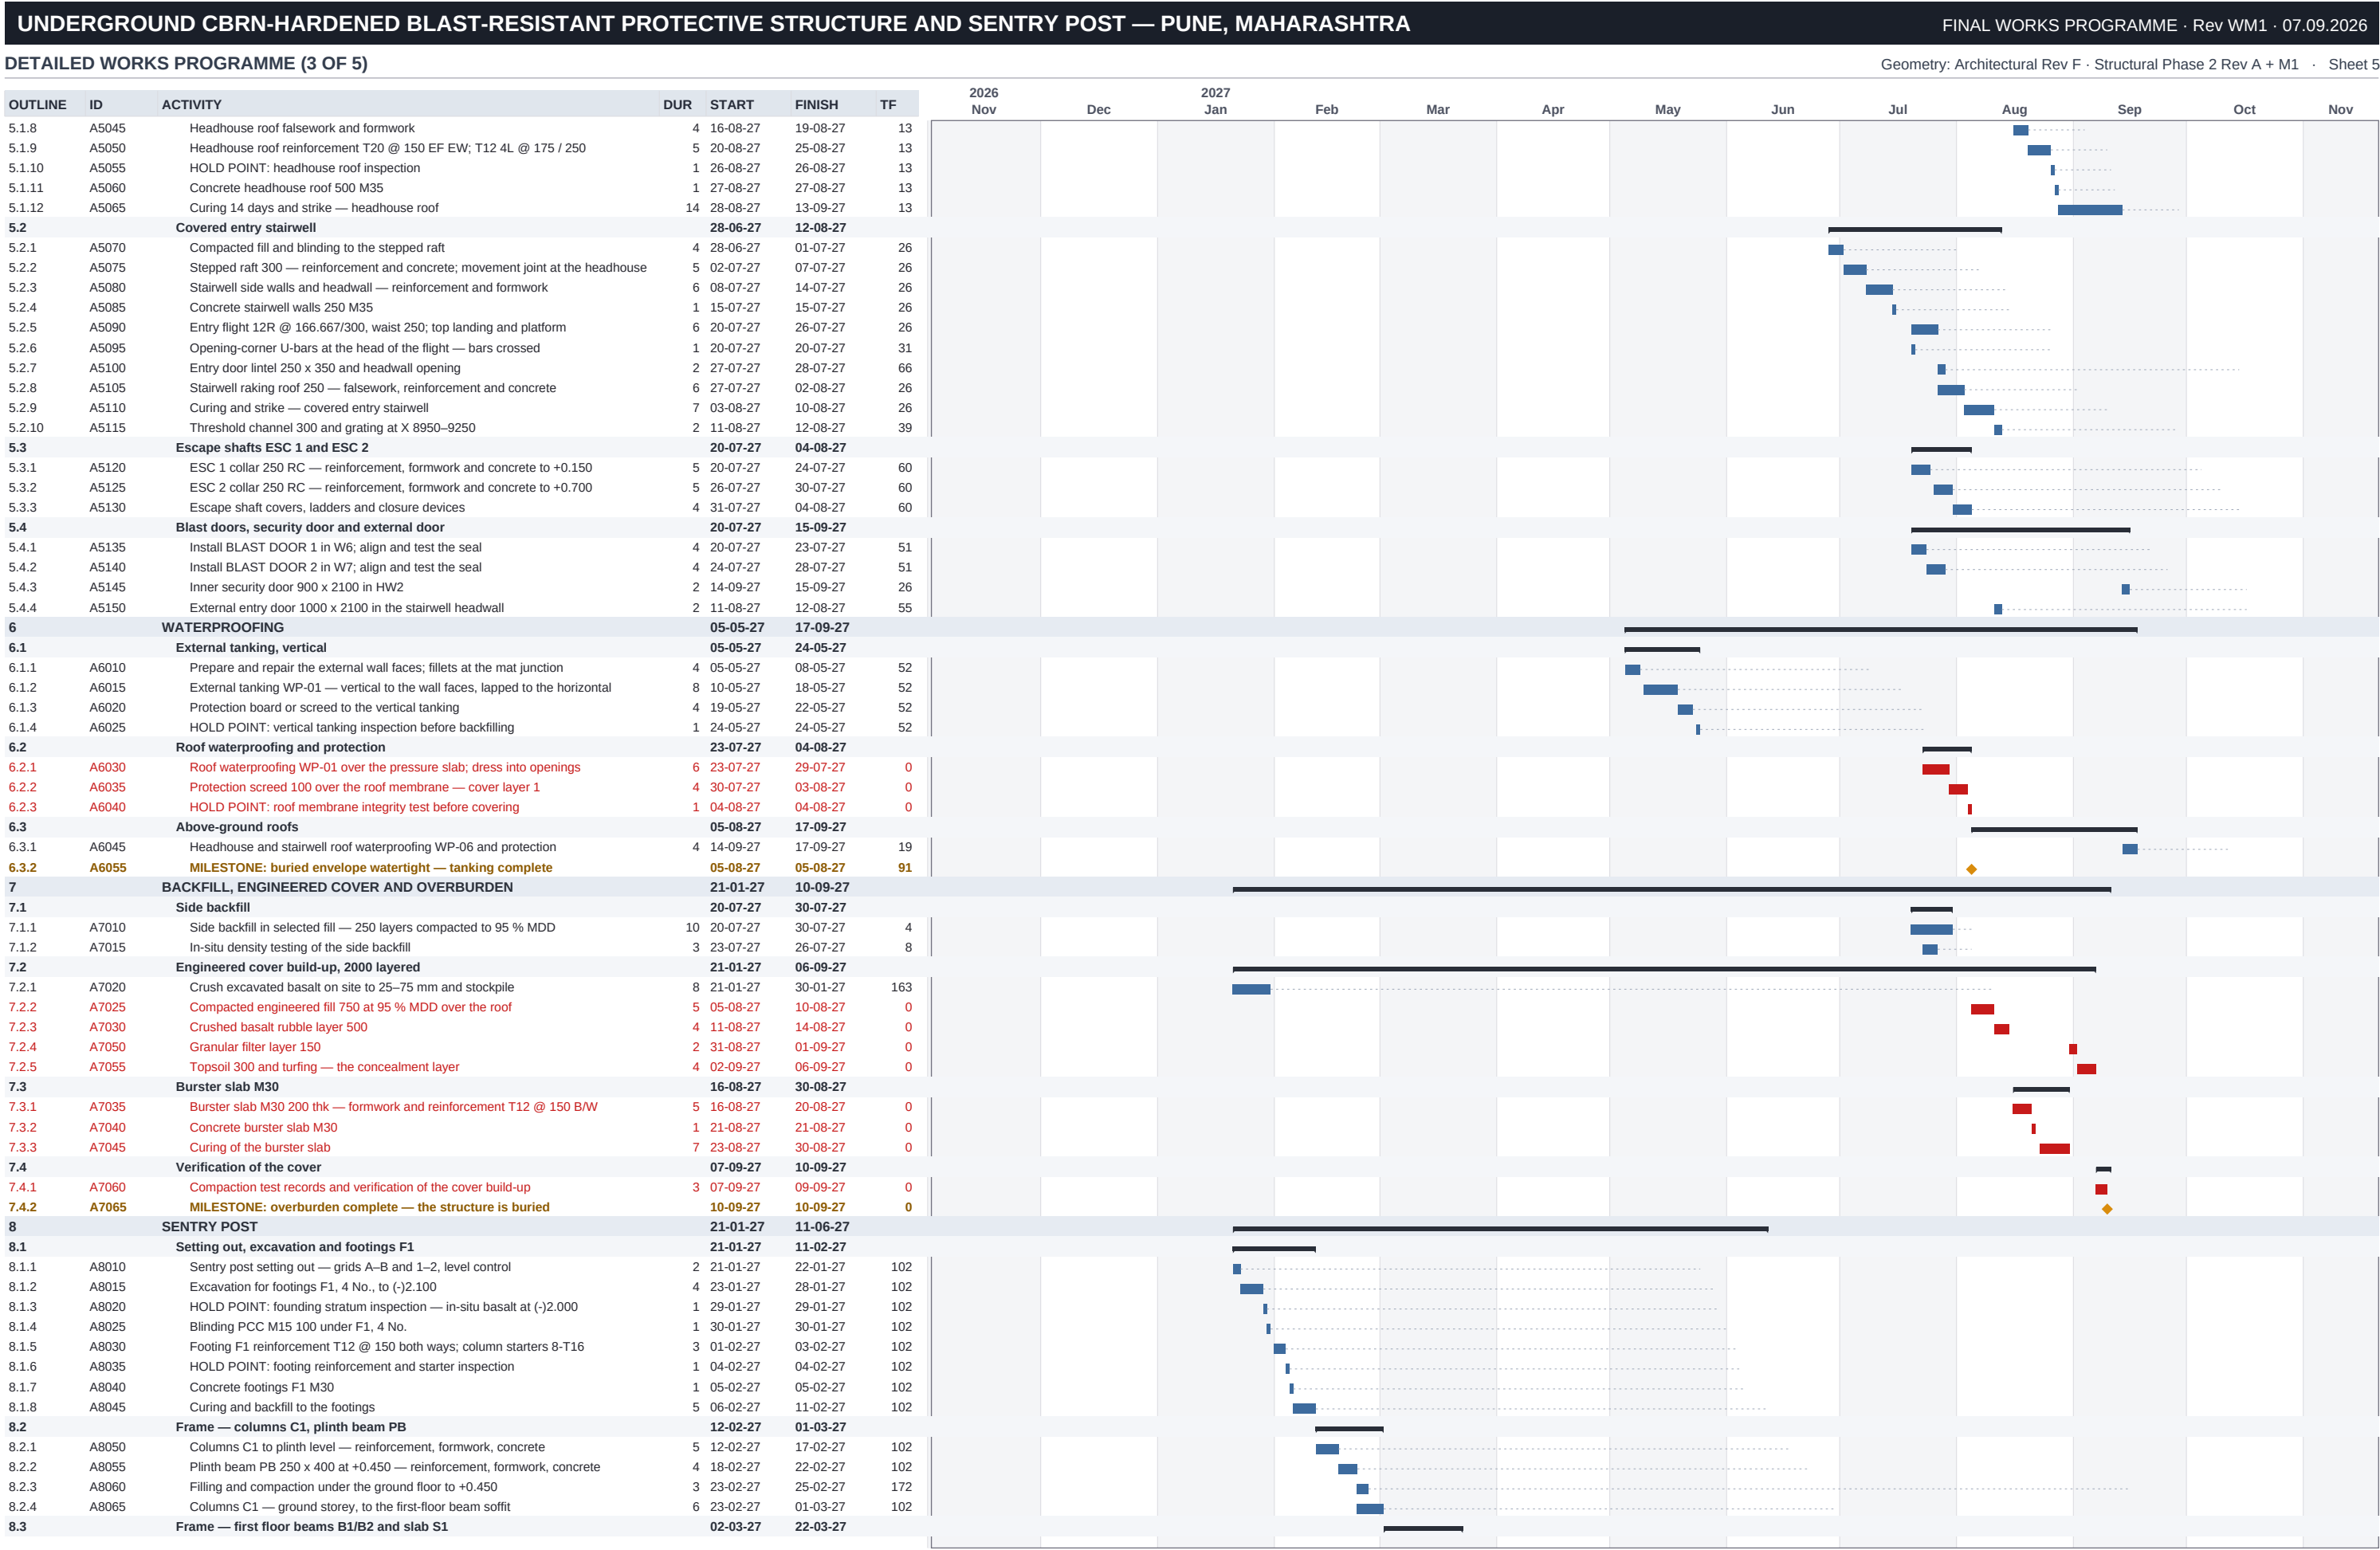

| UNDERGROUND CBRN-HARDENED BLAST-RESISTANT PROTECTIVE STRUCTURE AND SENTRY POST — PUNE, MAHARASHTRA |        |                                                                                  |          |          |          |     |                                                                                    |     |             | FINAL WORKS PROGRAMME · Rev WM1 · 07.09.2026                            |     |     |     |     |     |     |     |     |     |
|----------------------------------------------------------------------------------------------------|--------|----------------------------------------------------------------------------------|----------|----------|----------|-----|------------------------------------------------------------------------------------|-----|-------------|-------------------------------------------------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|-----|
| DETAILED WORKS PROGRAMME (4 OF 5)                                                                  |        |                                                                                  |          |          |          |     |                                                                                    |     |             | Geometry: Architectural Rev F · Structural Phase 2 Rev A + M1 · Sheet 6 |     |     |     |     |     |     |     |     |     |
| OUTLINE                                                                                            | ID     | ACTIVITY                                                                         | DUR      | START    | FINISH   | TF  | 2026<br>Nov                                                                        | Dec | 2027<br>Jan | Feb                                                                     | Mar | Apr | May | Jun | Jul | Aug | Sep | Oct | Nov |
| 8.3.1                                                                                              | A8070  | First floor beams B1/B2 and slab S1 150 — falsework and formwork                 | 5        | 02-03-27 | 06-03-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.3.2                                                                                              | A8075  | First floor beam and slab reinforcement, incl. corner torsion steel              | 4        | 08-03-27 | 11-03-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.3.3                                                                                              | A8080  | HOLD POINT: first floor reinforcement inspection — IS 13920 detailing            | 1        | 12-03-27 | 12-03-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.3.4                                                                                              | A8085  | Concrete first floor beams and slab M30                                          | 1        | 13-03-27 | 13-03-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.3.5                                                                                              | A8090  | Curing 7 days; strike sides, props to remain                                     | 7        | 15-03-27 | 22-03-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4                                                                                                |        | Frame — roof beams, slab, projection and parapet                                 | 23-03-27 | 20-04-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.1                                                                                              | A8095  | Columns C1 — first storey, to the roof beam soffit                               | 6        | 23-03-27 | 29-03-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.2                                                                                              | A8100  | Roof beams B1/B2 and slab S1 with the 300 projection — formwork and reinforce    | 6        | 30-03-27 | 05-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.3                                                                                              | A8105  | HOLD POINT: sentry post roof reinforcement inspection                            | 1        | 06-04-27 | 06-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.4                                                                                              | A8110  | Concrete sentry post roof M30                                                    | 1        | 07-04-27 | 07-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.5                                                                                              | A8115  | Parapet 300 high over the roof projection                                        | 3        | 12-04-27 | 14-04-27 | 186 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.6                                                                                              | A8120  | Curing and strike — sentry post roof                                             | 10       | 08-04-27 | 19-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.4.7                                                                                              | A8125  | MILESTONE: sentry post frame complete                                            | 20-04-27 | 20-04-27 | 182      |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5                                                                                                |        | BRICK MASONRY WALLS (design change SP-B1)                                        | 15-03-27 | 28-04-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5.1                                                                                              | A8130  | Brick delivery, stacking, sampling and testing to IS 3495                        | 4        | 15-03-27 | 18-03-27 | 121 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5.2                                                                                              | A8135  | BRICK MASONRY WALLS — ground storey, 190 thk in CM 1:6                           | 5        | 23-03-27 | 27-03-27 | 118 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5.3                                                                                              | A8145  | HOLD POINT: masonry line, level, plumb and joint thickness — ground storey       | 1        | 31-03-27 | 31-03-27 | 118 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5.4                                                                                              | A8150  | BRICK MASONRY WALLS — first storey, 190 thk in CM 1:6                            | 4        | 20-04-27 | 23-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5.5                                                                                              | A8160  | HOLD POINT: masonry inspection — first storey                                    | 1        | 27-04-27 | 27-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.5.6                                                                                              | A8165  | MILESTONE: sentry post brick masonry complete                                    | 28-04-27 | 28-04-27 | 175      |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.6                                                                                                |        | Lintels and openings                                                             | 29-03-27 | 26-04-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.6.1                                                                                              | A8140  | RC lintels over the D1 and W1 openings — ground storey                           | 2        | 29-03-27 | 30-03-27 | 118 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.6.2                                                                                              | A8155  | RC lintels over the vision panel and door openings — first storey                | 2        | 24-04-27 | 26-04-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.7                                                                                                |        | Spiral stair                                                                     | 20-04-27 | 26-04-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.7.1                                                                                              | A8170  | External spiral stair 1000 R, 250 dia central pole — fabrication and erection    | 6        | 20-04-27 | 26-04-27 | 147 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8                                                                                                |        | Plaster, flooring and finishes                                                   | 04-05-27 | 11-06-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.1                                                                                              | A8180  | Sentry post internal plaster 12 mm, sand faced, CM 1:4                           | 6        | 04-05-27 | 10-05-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.2                                                                                              | A8185  | Sentry post external plaster 15 mm, two coat, with scaffolding                   | 6        | 11-05-27 | 17-05-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.3                                                                                              | A8190  | Sentry post flooring — ground and first floor                                    | 4        | 11-05-27 | 14-05-27 | 110 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.4                                                                                              | A8195  | Door D1 (2 No.), window W1 and armoured vision panel installation                | 6        | 18-05-27 | 24-05-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.5                                                                                              | A8205  | Sentry post painting — internal and external                                     | 6        | 01-06-27 | 07-06-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.6                                                                                              | A8210  | Sentry post testing and snagging                                                 | 3        | 08-06-27 | 10-06-27 | 109 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.8.7                                                                                              | A8215  | MILESTONE: sentry post complete                                                  | 11-06-27 | 11-06-27 | 109      |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.9                                                                                                |        | Electrical installation                                                          | 28-04-27 | 31-05-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.9.1                                                                                              | A8175  | Sentry post electrical — conduits and boxes chased into the masonry              | 4        | 28-04-27 | 03-05-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 8.9.2                                                                                              | A8200  | Sentry post electrical — wiring, distribution board, fittings, earthing          | 6        | 25-05-27 | 31-05-27 | 102 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9                                                                                                  |        | MECHANICAL, CBRN AND HVAC SERVICES                                               | 20-03-27 | 26-08-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.1                                                                                                |        | Builder's work, sleeves and penetrations                                         | 20-03-27 | 26-03-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.1.1                                                                                              | A9010  | Builder's work — sleeves, ducts and penetrations coordinated with the RC         | 6        | 20-03-27 | 26-03-27 | 10  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.2                                                                                                |        | Shafts, ductwork and blast valves                                                | 17-06-27 | 09-08-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.2.1                                                                                              | A9015  | Install blast valve sleeves in the walls and roof                                | 4        | 17-06-27 | 21-06-27 | 74  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.2.2                                                                                              | A9020  | Fresh-air shaft SH-1 600 x 600 and gooseneck head at +1.500                      | 5        | 20-07-27 | 24-07-27 | 45  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.2.3                                                                                              | A9025  | Generator air shaft SH-2 600 x 600                                               | 4        | 20-07-27 | 23-07-27 | 46  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.2.4                                                                                              | A9030  | Ductwork installation, bays 1–6 — every run inspectable along its length         | 10       | 23-07-27 | 03-08-27 | 17  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.2.5                                                                                              | A9035  | Install blast valves BV-1 to BV-5                                                | 5        | 04-08-27 | 09-08-27 | 37  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.3                                                                                                |        | CBRN plant and generator                                                         | 24-07-27 | 26-08-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.3.1                                                                                              | A9040  | Install CBRN filter trains AHU-1 and AHU-2 in bay 5                              | 8        | 04-08-27 | 12-08-27 | 17  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.3.2                                                                                              | A9045  | Install CO2 scrubber, oxygen store and dehumidifier                              | 5        | 13-08-27 | 18-08-27 | 17  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.3.3                                                                                              | A9050  | Install generator GEN-1 15 kVA in bay 8 on a bundled plinth                      | 5        | 24-07-27 | 29-07-27 | 46  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.3.4                                                                                              | A9055  | HVAC terminal devices, dampers and controls                                      | 6        | 19-08-27 | 25-08-27 | 17  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 9.3.5                                                                                              | A9060  | MILESTONE: CBRN plant installed                                                  | 26-08-27 | 26-08-27 | 23       |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10                                                                                                 |        | DRAINAGE AND SANITARY WORKS                                                      | 23-07-27 | 16-09-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.1                                                                                               |        | Internal drainage and the clean sump                                             | 23-07-27 | 12-08-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.1.1                                                                                             | A10010 | Internal gullies GY-01 to GY-09; floor falls set out                             | 4        | 23-07-27 | 27-07-27 | 12  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.1.2                                                                                             | A10015 | Waste and effluent drains PD-01 and PD-03 — laid and tested                      | 5        | 28-07-27 | 02-08-27 | 12  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.1.3                                                                                             | A10020 | Clean sump SU-01 — fit out, pumps PU-01/PU-02 and hand pump PU-03                | 5        | 03-08-27 | 07-08-27 | 42  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.1.4                                                                                             | A10025 | Rising main PD-05 — isolation valve, gas-tight NRV, blast check valve and deep-s | 4        | 09-08-27 | 12-08-27 | 42  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.2                                                                                               |        | Segregated decontamination effluent                                              | 03-08-27 | 06-08-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.2.1                                                                                             | A10030 | Decontamination effluent segregation — CP-01 and tank TK-01 in bay 8             | 4        | 03-08-27 | 06-08-27 | 47  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3                                                                                               |        | Above-ground and external drainage                                               | 31-07-27 | 16-09-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.1                                                                                             | A10035 | Stairwell sump SU-02 and pumps PU-04/PU-05                                       | 4        | 11-08-27 | 14-08-27 | 40  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.2                                                                                             | A10040 | Headhouse gully GY-11 and trapped connection                                     | 2        | 14-09-27 | 15-09-27 | 13  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.3                                                                                             | A10045 | Threshold channel CH-10, catchpit CP-10 and connections                          | 3        | 13-08-27 | 16-08-27 | 39  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.4                                                                                             | A10050 | Septic tank ST-01 — excavation, construction and testing                         | 8        | 31-07-27 | 09-08-27 | 33  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.5                                                                                             | A10055 | Soak pits SK-01 and SK-02 — constructed after the percolation test               | 6        | 10-08-27 | 16-08-27 | 33  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.6                                                                                             | A10060 | External drainage connections and chambers                                       | 6        | 17-08-27 | 23-08-27 | 33  |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 10.3.7                                                                                             | A10065 | MILESTONE: drainage installed                                                    | 16-09-27 | 16-09-27 | 13       |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 11                                                                                                 |        | ELECTRICAL AND EMP WORKS                                                         | 15-03-27 | 02-09-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 11.1                                                                                               |        | Concealed containment and earthing                                               | 15-03-27 | 19-08-27 |          |     |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 11.1.1                                                                                             | A11015 | Earth pits, earth electrodes and the buried earth ring                           | 5        | 15-03-27 | 19-03-27 | 157 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| 11.1.2                                                                                             | A11020 | EMP straps and bonding at every construction joint                               | 8        | 09-04-27 | 17-04-27 | 138 |                                                                                    |     |             |                                                                         |     |     |     |     |     |     |     |     |     |
| LEGEND                                                                                             |        |                                                                                  |          |          |          |     | ■ WBS summary   ■ Activity   ■ Critical (TF = 0)   ■ Milestone   ..... Total float |     |             |                                                                         |     |     |     |     |     |     |     |     |     |

| UNDERGROUND CBRN-HARDENED BLAST-RESISTANT PROTECTIVE STRUCTURE AND SENTRY POST — PUNE, MAHARASHTRA |        |                                                                              |     |          |          |    |                                                                                    |     |             |     |     |     |     |     | FINAL WORKS PROGRAMME · Rev WM1 · 07.09.2026                            |     |     |     |     |
|----------------------------------------------------------------------------------------------------|--------|------------------------------------------------------------------------------|-----|----------|----------|----|------------------------------------------------------------------------------------|-----|-------------|-----|-----|-----|-----|-----|-------------------------------------------------------------------------|-----|-----|-----|-----|
| DETAILED WORKS PROGRAMME (5 OF 5)                                                                  |        |                                                                              |     |          |          |    |                                                                                    |     |             |     |     |     |     |     | Geometry: Architectural Rev F · Structural Phase 2 Rev A + M1 · Sheet 7 |     |     |     |     |
| OUTLINE                                                                                            | ID     | ACTIVITY                                                                     | DUR | START    | FINISH   | TF | 2026<br>Nov                                                                        | Dec | 2027<br>Jan | Feb | Mar | Apr | May | Jun | Jul                                                                     | Aug | Sep | Oct | Nov |
| 11.1.3                                                                                             | A11050 | Earthing conductors, bonding and connection to the electrode system          | 6   | 13-08-27 | 19-08-27 | 33 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.2                                                                                               |        | EMP Zone 2 enclosure and penetration protection                              |     | 23-07-27 | 05-08-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.2.1                                                                                             | A11025 | Main cable route, service entry plate and EMP penetration protection         | 6   | 23-07-27 | 29-07-27 | 12 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.2.2                                                                                             | A11030 | EMP Zone 2 shielded enclosure erection in bay 3 — SPECIALIST                 | 12  | 23-07-27 | 05-08-27 | 45 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.3                                                                                               |        | Distribution, lighting and power                                             |     | 30-07-27 | 02-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.3.1                                                                                             | A11035 | Distribution board, sub-mains and final circuit wiring                       | 12  | 30-07-27 | 12-08-27 | 12 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.3.2                                                                                             | A11040 | Lighting, small power and emergency lighting installation                    | 10  | 13-08-27 | 24-08-27 | 12 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.3.3                                                                                             | A11045 | Generator connection, changeover panel and protection                        | 5   | 13-08-27 | 18-08-27 | 34 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.3.4                                                                                             | A11055 | Power to pumps, fans, filter trains and controls                             | 6   | 26-08-27 | 01-09-27 | 17 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 11.3.5                                                                                             | A11060 | MILESTONE: electrical installation complete                                  |     | 02-09-27 | 02-09-27 | 22 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12                                                                                                 |        | INTERNAL FINISHES                                                            |     | 27-07-27 | 18-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.1                                                                                               |        | Substrate preparation and wet-area tanking                                   |     | 27-07-27 | 07-08-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.1.1                                                                                             | A12010 | Substrate preparation — hack, make good, prepare soffits and walls           | 6   | 27-07-27 | 02-08-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.1.2                                                                                             | A12015 | Internal wet-area tanking WP-04 — bays 2, 5 and 6                            | 5   | 03-08-27 | 07-08-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2                                                                                               |        | Floor finishes and skirtings                                                 |     | 09-08-27 | 17-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.1                                                                                             | A12020 | Floor screeds laid to falls, bays 1–8                                        | 8   | 09-08-27 | 17-08-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.2                                                                                             | A12025 | Floor finish F-01 — sealed power-floated, bays 1, 3 and 4                    | 6   | 18-08-27 | 24-08-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.3                                                                                             | A12030 | Floor finish F-02 — seamless coved wet-area, bays 2, 5 and 6                 | 5   | 18-08-27 | 23-08-27 | 8  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.4                                                                                             | A12035 | Floor finish F-03 — non-slip, stair shaft, treads and landings               | 4   | 18-08-27 | 21-08-27 | 43 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.5                                                                                             | A12040 | Floor finish F-04 — oil-resistant with a banded plinth, bay 8                | 3   | 18-08-27 | 20-08-27 | 77 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.6                                                                                             | A12045 | Floor finish F-05 headhouse and F-06 covered entry stairwell                 | 4   | 14-09-27 | 17-09-27 | 53 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.2.7                                                                                             | A12050 | Coved skirtings S-01 / S-02, integral with the floor                         | 5   | 25-08-27 | 30-08-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.3                                                                                               |        | Wall and soffit finishes                                                     |     | 31-08-27 | 17-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.3.1                                                                                             | A12055 | Wall finishes W-01 / W-02 / W-03 — sealed washable coatings                  | 10  | 31-08-27 | 10-09-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.3.2                                                                                             | A12060 | Soffit finishes C-01 / C-02 — exposed RC, sealed                             | 6   | 11-09-27 | 17-09-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.4                                                                                               |        | Internal doors                                                               |     | 11-09-27 | 18-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.4.1                                                                                             | A12065 | Internal doors D-04 in the W8 partitions; gas-tight door D-05 in W5          | 4   | 11-09-27 | 15-09-27 | 55 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 12.4.2                                                                                             | A12070 | MILESTONE: internal finishes complete                                        |     | 18-09-27 | 18-09-27 | 53 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13                                                                                                 |        | EXTERNAL WORKS, CONCEALMENT AND RESTORATION                                  |     | 10-09-27 | 18-10-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.1                                                                                               |        | Berm, regrading and surface water                                            |     | 10-09-27 | 30-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.1.1                                                                                             | A13010 | Berm forming and grading 1.5:1 to +0.900 against the headhouse and stairwell | 8   | 10-09-27 | 18-09-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.1.2                                                                                             | A13015 | Site regrading — crown and falls 1:50 away from the structure                | 5   | 20-09-27 | 24-09-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.1.3                                                                                             | A13020 | Surface water drainage, cut-off drains and outfalls                          | 5   | 25-09-27 | 30-09-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.2                                                                                               |        | Access and hardstanding                                                      |     | 25-09-27 | 09-10-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.2.1                                                                                             | A13025 | Access route, hardstanding and turning area                                  | 8   | 25-09-27 | 05-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.2.2                                                                                             | A13030 | Sentry post surround, apron and drainage                                     | 4   | 06-10-27 | 09-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.3                                                                                               |        | Concealment and camouflage                                                   |     | 25-09-27 | 09-10-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.3.1                                                                                             | A13035 | Turfing and planting over the cover — the concealment layer                  | 6   | 25-09-27 | 01-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.3.2                                                                                             | A13040 | Camouflage and concealment — spoil dressing, track discipline, screening     | 6   | 04-10-27 | 09-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.4                                                                                               |        | Site restoration                                                             |     | 11-10-27 | 18-10-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.4.1                                                                                             | A13045 | Removal of temporary works, site restoration and clearing                    | 6   | 11-10-27 | 16-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 13.4.2                                                                                             | A13050 | MILESTONE: external works and concealment complete                           |     | 18-10-27 | 18-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14                                                                                                 |        | TESTING, COMMISSIONING AND HANDOVER                                          |     | 05-08-27 | 20-11-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.1                                                                                               |        | Structural verification                                                      |     | 23-08-27 | 23-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.1.1                                                                                             | A14010 | Concrete cube results at 28 days, all pours — review and acceptance          | 5   | 23-08-27 | 27-08-27 | 38 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.1.2                                                                                             | A14015 | Non-destructive testing — ultrasonic pulse velocity and rebound hammer       | 4   | 28-08-27 | 01-09-27 | 38 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.1.3                                                                                             | A14020 | Dimensional and as-built survey of the completed structure                   | 5   | 10-09-27 | 15-09-27 | 26 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.1.4                                                                                             | A14025 | Watertightness inspection of the completed envelope                          | 5   | 18-09-27 | 23-09-27 | 19 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.2                                                                                               |        | Services testing                                                             |     | 20-08-27 | 21-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.2.1                                                                                             | A14030 | Drainage testing — pipes, gullies, chambers, pump duty and standby           | 5   | 16-09-27 | 21-09-27 | 13 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.2.2                                                                                             | A14035 | Electrical testing — insulation, continuity, polarity, protection            | 5   | 02-09-27 | 07-09-27 | 33 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.2.3                                                                                             | A14040 | Earth resistance measurement — 5 ohm target                                  | 2   | 20-08-27 | 21-08-27 | 47 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.3                                                                                               |        | Protective-system testing                                                    |     | 05-08-27 | 28-09-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.3.1                                                                                             | A14045 | EMP shielding effectiveness survey — 80 dB, 10 kHz to 1 GHz                  | 8   | 18-09-27 | 27-09-27 | 8  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.3.2                                                                                             | A14050 | Blast doors 1 and 2 — functional and seal testing                            | 4   | 18-09-27 | 22-09-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.3.3                                                                                             | A14055 | Escape shaft access and closure functional test                              | 2   | 05-08-27 | 06-08-27 | 60 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.3.4                                                                                             | A14065 | Gas-tightness and overpressure test of the envelope, bays 1–6                | 5   | 23-09-27 | 28-09-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.4                                                                                               |        | Commissioning                                                                |     | 19-08-27 | 06-10-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.4.1                                                                                             | A14060 | HVAC and CBRN filter train commissioning — airflow and overpressure          | 8   | 02-09-27 | 10-09-27 | 17 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.4.2                                                                                             | A14070 | Generator load test and changeover proving                                   | 3   | 19-08-27 | 21-08-27 | 39 |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.4.3                                                                                             | A14075 | Integrated systems commissioning — protective mode operation                 | 6   | 29-09-27 | 06-10-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5                                                                                               |        | Completion and handover                                                      |     | 07-10-27 | 20-11-27 |    |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.1                                                                                             | A14080 | Snagging inspection and defects list                                         | 5   | 18-10-27 | 22-10-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.2                                                                                             | A14085 | Rectification of defects                                                     | 10  | 23-10-27 | 03-11-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.3                                                                                             | A14090 | As-built drawings, O&M manuals and test certificates                         | 12  | 07-10-27 | 20-10-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.4                                                                                             | A14095 | Operator training — CBRN plant, pumps, generator, doors, escape shafts       | 5   | 21-10-27 | 26-10-27 | 7  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.5                                                                                             | A14098 | Programme contingency — festival holidays and weather allowance              | 10  | 04-11-27 | 15-11-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.6                                                                                             | A14100 | Final inspection and handover documentation                                  | 4   | 16-11-27 | 19-11-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| 14.5.7                                                                                             | A14105 | MILESTONE: PRACTICAL COMPLETION AND HANDOVER                                 |     | 20-11-27 | 20-11-27 | 0  |                                                                                    |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
| LEGEND                                                                                             |        |                                                                              |     |          |          |    | ■ WBS summary   ■ Activity   ■ Critical (TF = 0)   ■ Milestone   ..... Total float |     |             |     |     |     |     |     |                                                                         |     |     |     |     |
